


Construction Notice

SAINT PAUL DOWNTOWN AIRPORT (HOLMAN FIELD)

2025 PERIMETER ROADS & TAXIWAY B RECONSTRUCTION

Project Background

The Metropolitan Airports Commission (MAC) will complete the rehabilitation of Eaton Street (south of Gate A), along with the reconstruction of Taxiway B and portions of Taxiways A2 and A3 this year. For the taxiway portion of the project, crews will reclaim and recycle the existing pavement structure to produce a new aggregate base for the reconstructed pavement section. The rehabilitation of Eaton Street will include a partial mill and overlay of the existing bituminous pavement to extend its useful life. This project is anticipated to begin on July 7, coinciding with the ongoing Runway 14/32 Reconstruction project.

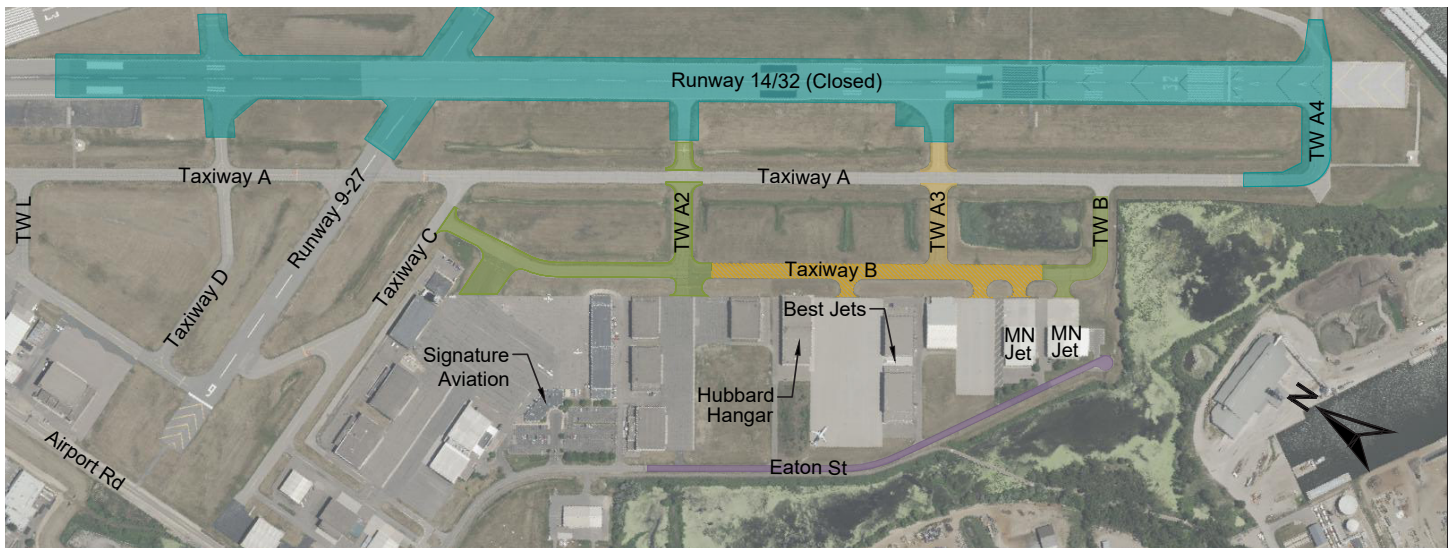

Schedule

Project is scheduled to occur between July 7, 2025 - Aug. 9, 2025

The project is anticipated to be completed by **Aug. 9, 2025**.

Note: The construction is weather dependent and the dates listed are subject to change if inclement weather conditions occur. Check NOTAMs daily.



Construction Impact

- Phase 1 - Taxiway B & A2 Reconstruction**
12 Working Days (July 7 - July 19)
 - Closures: Taxiway B (between Taxiway A2 and C, and between Taxiway A and MN Jet), Taxiway A2.
- Phase 2 - Taxiway B & A3 Reconstruction**
12 Working Days (July 21 - Aug. 2)
 - Closures: Taxiway B (between Taxiway A2 and MN Jet).
- Phase 3 - Eaton Street**
6 Working Days (Dates TBD, after Aug. 4)
 - Note: Crews will maintain one way traffic as able during construction.
- Runway 14/32 Reconstruction**
(Occuring Concurrently, June 2 - Aug. 9)



Contact

Lindsay Reidt, PE
SEH (Engineer)
763.370.4055

Kyle Nelson, PE
SEH (Engineer)
651.900.0016

Blaine Peterson
STP Airport Manager
612.467.0931

Contractor:
Max Steining, Inc.

