



Lake Elmo Airport

CONSTRUCTION NEWS



Learn More:

Project newsletters including construction updates and photos will be posted regularly during construction on the airport website.

<https://metroairports.org/lake-elmo-airport-construction>

Long Term Comprehensive Plan (LTCP):

<https://metroairports.org/lake-elmo-ltcp-2035-project-documents>

Environmental Assessment/Environmental Assessment Worksheet (EA/EAW):

<https://metroairports.org/lake-elmo-environmental-assessment-worksheet-2018>

If you have questions about the project, please contact us via email at

ContactLakeElmoAirportEA@mspmac.org

PROJECT UPDATE:


Significant progress has been made on the Runway 14/32 Replacement project throughout the month of September. The focus for construction the past month has been on completing the filtration basins and constructing taxiways. The new taxiways have been paved and will be painted and opened in early October. All green spaces and edges adjacent to opening pavements were graded and will be seeded prior to the opening of the new taxiways.

The contractor has also spent the month of September working on grading related to storm water management. Installation of all the pond and basins are complete. An evaporator was installed in Pond 1 and is in test mode. The remaining evaporators will be installed in the spring. [A fact sheet is available here](#) to learn more about this project's storm water management.

Work items for the remainder of the fall include constructing the North Service Road through aggregate base. Taxiway Bravo will be reconstructed at the Taxiway Echo intersection. All green space will have final restoration complete before winter.

The Precision Approach Path Indicators (PAPIs) and Runway End Identifier Lights (REILs) are currently being installed. Once installed, the FAA will flight check the new equipment prior to putting it into service.

The remainder of 30th Street, per the red hatch on the next page, will be reconstructed in 2023.

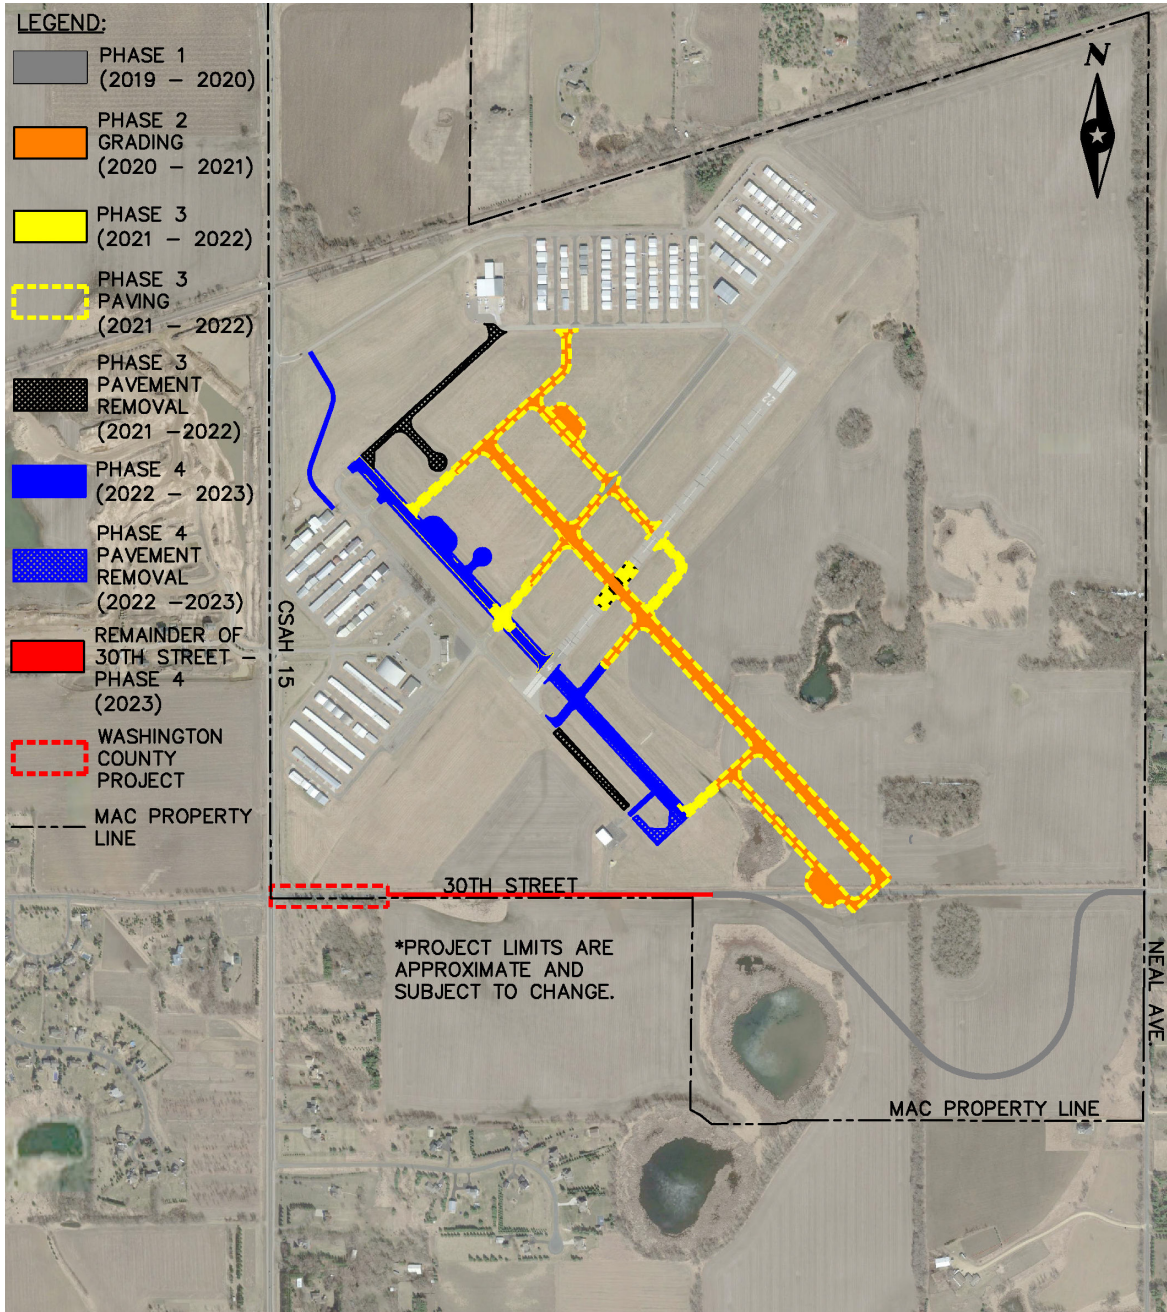

PROJECT SCHEDULE

phase
1

Realign 30th Street N
Complete.
Project close-out in process.

phase
2

Runway 14/32 Replacement
& Airfield Modifications
Complete
Project close-out in process.

phase
3

Runway 14/32 Replacement
**Fall 2021 through
Fall 2022**
Completion of new Runway 14/32
and new taxiways.

phase
4

Runway 14/32 Replacement
**Fall 2022 through
Summer 2023**
Completion of taxiway
modifications, conversion of
existing runway to parallel taxiway,
and service roads.
Installation of NAVAIDS.
