



Lake Elmo Airport

CONSTRUCTION NEWS



Learn More:

Project newsletters including construction updates and photos will be posted regularly during construction on the airport website.

<https://metroairports.org/lake-elmo-airport-construction>

Long Term Comprehensive Plan (LTCP):

<https://metroairports.org/lake-elmo-ltcp-2035-project-documents>

Environmental Assessment/Environmental Assessment Worksheet (EA/EAW):

<https://metroairports.org/lake-elmo-environmental-assessment-worksheet-2018>

If you have questions about the project, please contact us via email at

ContactLakeElmoAirportEA@mspmac.org


PROJECT UPDATE:

Construction for Phase 3 of the runway replacement project started again on May 23rd. The contractor has been working on stripping topsoil in preparation for grading. Taxiways Golf and Delta are the primary focus along with grading Basin 2 and Pond 2. The electrical contractor has also been on-site installing base cans for edge lights and pads for airfield guidance signs.

Activities expected this next month are the continuation of grading taxiways and the runway. The closure of Runway 4-22 is expected to happen the week after Memorial Day. The duration of the closure will be approximately one month.

During this time, the contractors will be preparing the intersection of the runways and taxiways. Import of select granular and aggregate base will take place once subgrade soils are prepared. Once complete, the contractor will pave the new runway along with associated taxiways.

Upon completion of the new runway the work in the vicinity of the existing runway will continue. This includes installing the storm water features such as basins, ponds and evaporators. [A fact sheet is available here](#) to learn more about this project's storm water management. Exact dates of the new runway opening are to be determined, but it is currently anticipated that it will be open later this summer.

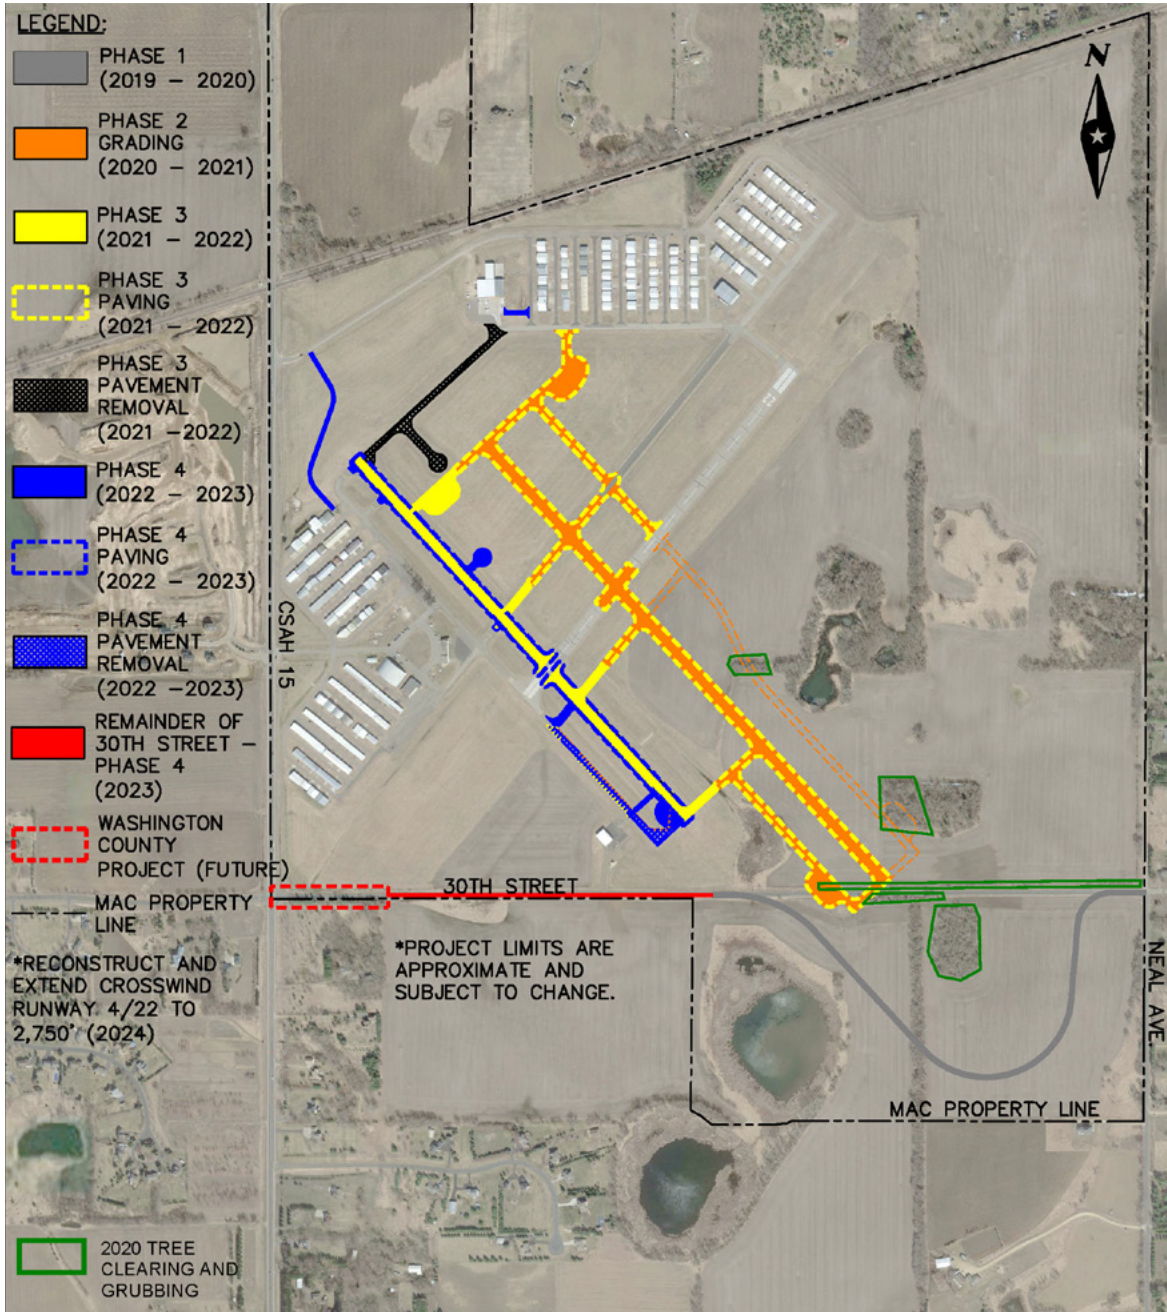

PROJECT SCHEDULE

phase
1

Realign 30th Street N
Complete.
Project close-out in process.

phase
2

Runway 14/32 Replacement & Airfield Modifications
Substantially complete.

Punchlist items and project close-out in process.

phase
3

Runway 14/32 Replacement
Fall 2021 through Summer 2022

Completion of new Runway 14/32 and new taxiways.

phase
4

Runway 14/32 Replacement
Fall 2022 through Summer 2023

Completion of taxiway modifications, conversion of existing runway to parallel taxiway, and service roads.
